MapKMigGon38571: one ticket, three kinds of work

Triage lanes by domain, owner and source (Work · Queue) · currently 8 SP, Waiting for QA

For: Project Manager · From: Andrés Serrón (developer) · 14 October 2026

8 SP
Size in Singular Stories today (the AI suggestion was 5)

13 SP
Proposed size (5 + 5 + 3)

41
Acceptance criteria traced: 38 met, 3 not applicable

4 days
Working days from In Progress to Waiting for QA (Oct 8 to 13)

Decisions requested from the PM

1. Re-size MapKMigGon38571 from 8 to 13 SP so the points match the scope that was delivered.
2. Adopt *split before sizing*: one story per kind of work (Hyperagent, Airtable data + automation, Airtable interface), one view per interface story, each capped at 5 SP.
3. Apply the same review to the other Command Center stories before sprint close, starting with MapKMigGon38570 (Today, 8 SP).

The short version

The title reads like a filtered list. The delivered work is three things in one: a small triage engine in Airtable (three new tables, rules and an hourly automation), a Work · Queue page with 17 front-end behaviors that each had to be built, tested and verified, and the verification package itself. Singular Stories gives a story a single number whatever its content: a view with 3 behaviors and a view with 17 land in the same point range. This review shows where the 8 under-counts the work, how points map to delivery time, and a way to size each concern on its own so the totals stay honest.

1. One ticket, three kinds of work

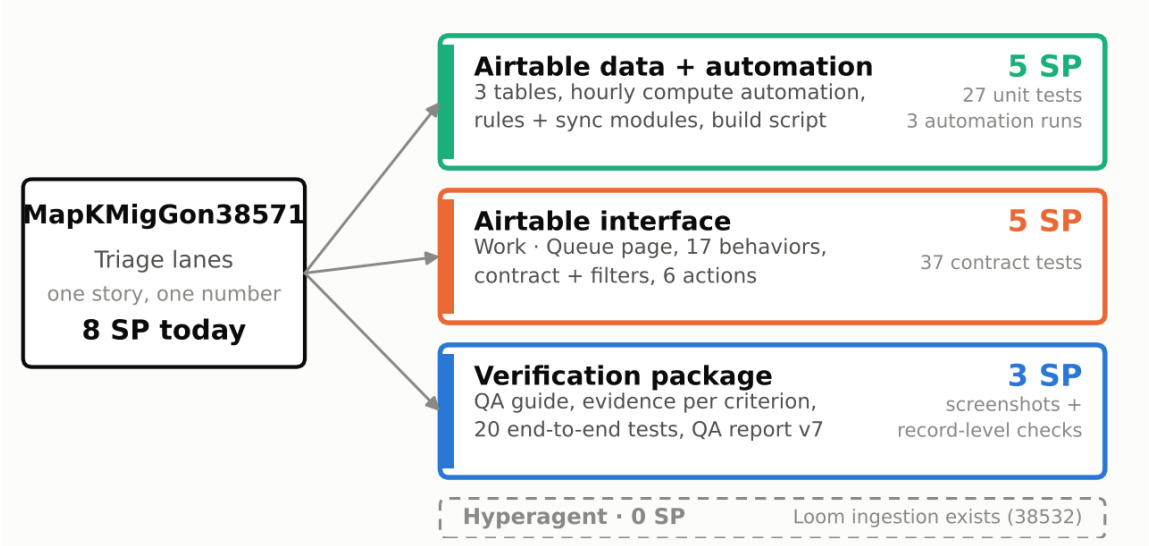


Figure 1. How the story divides by concern. The 5 + 5 + 3 split is the proposed sizing of the delivered scope; the Hyperagent slice is empty here because ingestion already existed (MapKMigGon38532) and this story adds no new AI.

The slices differ in content, tests and risk. The data slice is verified with unit tests and automation runs. The interface slice is verified with screenshots: an Airtable custom component runs in a cross-origin iframe with no DOM access, so every write is checked record by record.

2. What was actually delivered

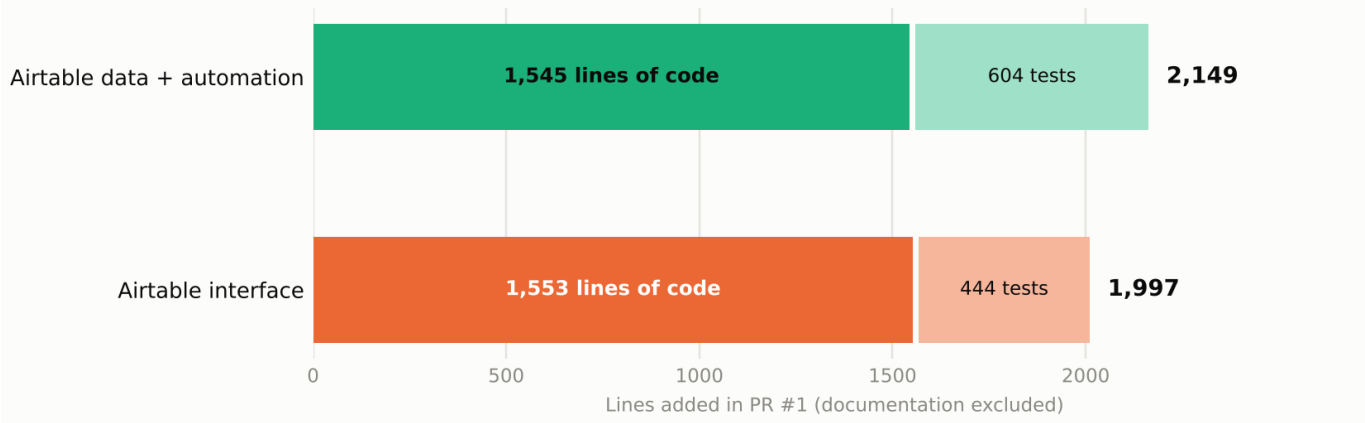


Figure 2. Lines added by the merged pull request (PR #1, 23 commits, 38 files), split by slice. Documentation is excluded (1,696 further lines). The two build slices come out close in size, which is why each is sized at 5.

Measure	Evidence
Acceptance criteria	41 traced to the real stack: 38 met, 3 not applicable (D5, E4, S2), 9 documented gaps, none blocking QA.
Starting point	Only 8 of 41 criteria were met when the work started. The earlier work had been built against a different AC (CC4), and the Work · Queue source file was not in the repository.
Data model	3 new tables (triage rows, triage config, team roster); data-panel setup for 6 tables; custom-component write permissions.
Code and tests	3,058 lines of source and 1,048 lines of tests. 64 unit tests (rules 13, sync 10, compute 4, contract 37), 3 automation runs and 20 end-to-end tests.
Verification	QA report v7, 23 pages, plus a QA guide so the QA engineer can repeat the tests. Three QA rounds found defects that no unit test could.
Design rework	v1.1 planned formulas in Airtable; v2 replaced them with an hourly script and a table of its own, adding a module, a table and an automation.
Client dependencies	Four decisions belong to the client (stale rule, default lane, delegation roster, owner map). The roster is still empty.

Plan estimate for the work was 26 hours (v2.2, down from 29.5 hours in v1.1). Hours actually worked were not tracked, so this review uses scope and elapsed days, not hours.

Related stories in the same epic

Story	View	Points	Status in SS
MapKMigGon38569	CEO dashboard	5	Finished after QA
MapKMigGon38570	Today / On Fire	8	Waiting for QA
MapKMigGon38571	Work · Queue	8 (proposed 13)	Waiting for QA

3. How points map to time, and how to size each slice

Singular Stories converts points into delivery days with fixed tiers. A story is 0 to 16 points; bigger stories must be split. I read the tiers by querying the estimator at 1, 2, 3, 4, 5, 6, 8, 10, 13 and 16 points.

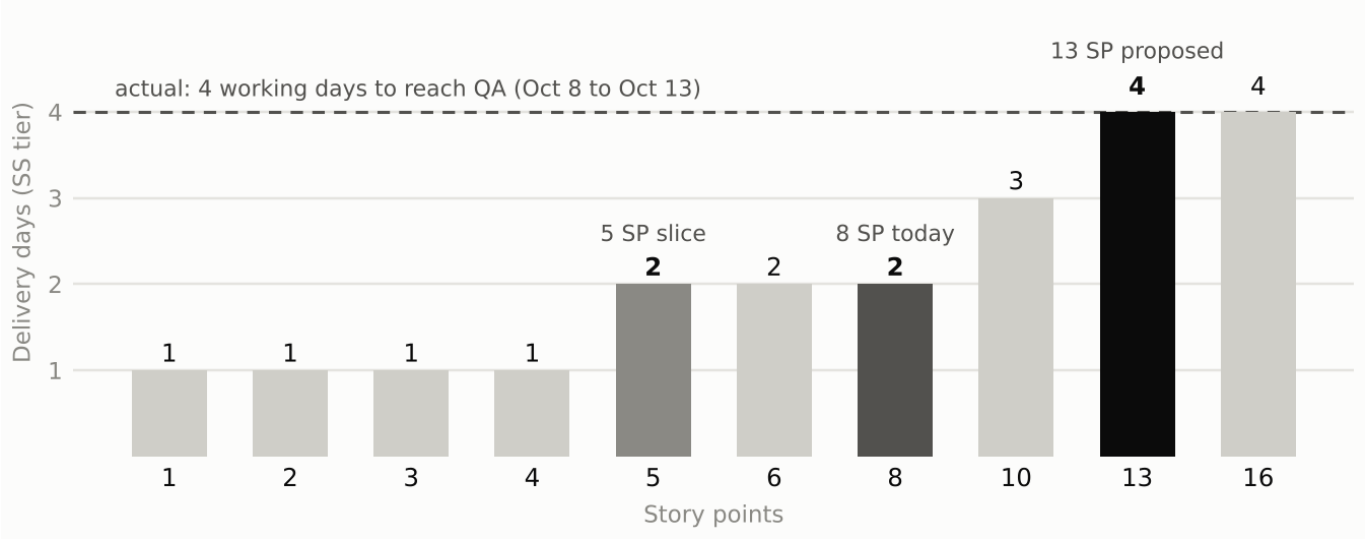


Figure 3. Delivery days by story points. An 8 gets the same two days as a 5, yet the story took four working days to reach QA. Either two slices of 5 (2 + 2 days) or a single 13 (4 days) match what happened.

A rubric for sizing a slice

This is a proposal, not an SS rule. SS does not publish a sizing rubric; the only fixed rule I can measure is the tier table above.

Step	What to do
1. Split	Divide by concern first: Hyperagent, Airtable data + automation, Airtable interface. One view per interface story.
2. Count	List the verifiable behaviors in the slice and weight them: display-only is small, an interaction is medium, a write that needs server-side verification or a cross-source data rule is large.
3. Add fixed costs	View scaffold, data-panel and permission setup, and the QA evidence package. On Airtable custom components the QA package is heavy.
4. Map and cap	Map the total to the tier table. A slice above 5 SP is split again.

Rubric applied to MapKMigGon38571

Driver	Airtable data + automation	Airtable interface
Behaviors to verify	5 rule areas (owner match, lane, stale, delegation, cross-source identity) plus the diff planner	17 front-end behaviors, 3 individual and 3 bulk actions
Data objects	3 new tables, config, heartbeat	None new; reads 6 tables
Automation	1 hourly compute automation, build script	None
Writes to verify	Automation writes (dry run, live load, repeat runs)	Lane and event writes, checked record by record
Verification	27 unit tests, 3 automation runs	37 contract tests, screenshots
External dependency	4 client decisions (defaults shipped as config)	Airtable permission toggles
Result	**5 SP**	**5 SP (verification package, 3 SP, sized separately)**

4. Options and recommendation

Option	What changes	Trade-off
A. Re-size in place (recommended)	MapKMigGon38571 goes from 8 to 13 SP, recorded as calibration; split-before-sizing applies from now on.	Simple, fits the story's actual scope. Changes the points of a story already in QA, so the PM decides.
B. Keep 8 SP	No change to this story; apply the split rule only to future stories.	No change to the story in QA, but the under-sizing stays on record and shapes the next estimates.
C. Split retroactively	Create three stories in SS (data + automation, interface, verification) and move the work across.	Cleanest tracking, heaviest admin for a story that is already built and in QA.

Next steps

#	Step	Owner
1	Decide between options A, B and C.	PM
2	If A or C: update the points in SS and add a comment with this report attached.	Andrés, after approval
3	Review MapKMigGon38570 (Today, 8 SP) with the same rubric before sprint close.	PM and Andrés
4	Add Airtable custom-component costs to the estimation checklist: data-panel setup, server-side checks of every write, screenshot evidence.	PM

Limits of this review

Points are relative to the team's calibration, which I do not have, so none of this converts points to hours. The count of 17 front-end behaviors is mine; the repository traces 41 acceptance criteria across all layers, and the two counts are not the same thing. How the AI suggestion of 5 was produced is not visible in SS. Lines of code are a weak proxy for effort, and part of the speed came from AI-assisted generation, which raises lines per hour. About 40% of the pull request is documentation and QA evidence. The delivery days come from the SS scheduling tiers and are not a measure of effort.

Sources

Repository aserron-sa/mapking-dev: pull request #1 (merged 2026-10-13), stories/MapKMigGon38571 (spec 2.0, evidence, QA guide, implementation plan, estimation report). Singular Stories: story details for 38569, 38570 and 38571; delivery-day estimator. Drive: MapKMigGon38571-sizing-report (2026-10-13) and MapMigGon37539 re-estimation plan (2026-10-13).
